Project Management - IS/IT

Duration : 8 bulan
Industry : HR - ERP (IS/IT)

Project Charter

Project Title : ERP Human Resource Management System (HRIS)

Project Start Date : 12 August 2024
Project Finish Date : 10 April 2025

Project Objectives :

Implementasi proyek ERP dari perusahaan kami ke perusahaan *client* melibatkan penyebaran dan integrasi solusi perangkat lunak yang komprehensif di seluruh organisasi. Sistem ini memungkinkan sentralisasi data dan proses, meningkatkan visibilitas dan aksesibilitas data, serta otomatisasi tugas dan alur kerja rutin. Proyek HRIS (Sistem Informasi Sumber Daya Manusia) bertujuan untuk menyederhanakan proses SDM, meningkatkan akurasi dan aksesibilitas data, serta meningkatkan manajemen tenaga kerja secara keseluruhan. Fokus utamanya adalah untuk mengotomatiskan fungsi SDM utama, termasuk administrasi penggajian dan tunjangan, perekrutan, dan manajemen kinerja.

Proyek ini juga berupaya untuk memastikan kepatuhan terhadap persyaratan hukum dan peraturan, memungkinkan pengambilan keputusan berdasarkan data melalui pelaporan dan analitik yang kuat, dan mendukung tujuan strategis organisasi melalui manajemen bakat yang efektif dan inisiatif keterlibatan karyawan.

Key Schedule Milestones :

- *User Requirement* Selesai paling lambat 10 Oktober 2024.
- Implementasi *ERP* Selesai paling lambat 26 Desember 2024.
- Melaksanakan *System Testing* Selesai paling lambat 29 Januari 2025.
- Mengumpulkan Dokumentasi untuk pengguna selesai paling lambat 25 Februari 2025.
- Melaksanakan Uji Coba dari Pengguna Selesai paling lambat 29 Maret 2025 Penyelesaian Pekerjaan Selesai paling lambat.
- Penyelesaian Project selesai paling lambat 10 April 2025.

Budget Information :

Perusahaan mengalokasikan sekitar 500jt untuk *development project* ini. Diluar budget ini, ada budget untuk membayar karyawan secara *reguler* (melalui *payroll*).

Project Manager : Mr. ERP

Main Project Success Criteria :

- **Streamlined Business Processes :**
  Pengimplemntasian ERP berusaha untuk menstandarisasi dan mengoptimalkan bisnis proses di berbagai departemen. Ini dapat menghapuskan redudansi dan inefisiensi yang akan mengarah ke operasi yang lebih lancar
- **Data Integration :**
  Tujuan utama adalah untuk melakukan menyatukan data dari berbagai area fungsional, kemungkinan pandangan holistik performa suatu organisasi. Ini akan mengarah ke peningkatan akurasi data dan pengambilan keputusan yang lebih baik
- **Improved Decision-Making :**
  Sistem ERP memberikan data dan analisa secara real time, memungkinkan bagi manajemen untuk membuat keputusan yang tepat dengan cepat. Ini akan memberikan pengambilan keputusan yang lebih tangkas dan berbasis data
- **Cost Reduction :**

Dengan melakukan otomasi proses manual yang sudah ada dan mengurangi error data, sistem ERP dapat mengurangi biaya operasi. Hal ini dapat mencakup pengurangan biaya tenaga kerja, mengurangi kelebihan inventori, atau mengoptimalkan supply chain.

- **Enhanced Customer Service :**
  Dengan data pelanggan dan alat komunikasi yang terintegrasi, organisasi dapat memberikan layanan pelanggan yang lebih baik dan menanggapi pertanyaan atau masalah secara lebih efektif.
- **Compliance and Reporting :**
  Sistem ERP organisasi memenuhi kepatuhan persyaratan dengan memastikan laporan keuangan dan operasional secara akurat dan tepat waktu.

Approach :

- Pertama, memastikan *requirement* dengan *stakeholder*, outputnya adalah suatu *Functional Requirement Document* (FRD).
- Kemudian mendevelop sistem berdasarkan FRD.
- Setelah sistem selesai di develop, akan dilakukan *User Acceptance Testing* (UAT) untuk memastikan sistem sesuai kebutuhan sebelum di *deliver*.
- *Training* kepada pengguna berdasarkan *training checklist* yang disiapkan.
- Setelah itu "*go live*" sistem yang telah diimplementasikan.

Roles and Responsibilities :

Role	Position	Responsibilities
Chief Financial Officer	Chief Financial Officer	Mengurus pembiayaan project jika terdapat add-ons feature diluar dari hasil pembahasan requirement yang telah ditetapkan dengan client.
Chief Operating Officer	Chief Operating Officer	Memastikan keseluruhan project dapat dimulai dan diselesaikan dengan baik.
Consultant	Consultant	Memberikan arahan strategis dalam pemilihan dan integrasi modul HRIS yang mendukung pengambilan keputusan berbasis data, efisiensi operasional, serta kepatuhan hukum. Mengarahkan tim terhadap praktik terbaik dalam otomatisasi fungsi SDM seperti payroll, rekrutmen, dan manajemen kinerja. Memberikan masukan dalam memastikan sistem mendukung inisiatif strategis seperti manajemen bakat dan keterlibatan karyawan. Menyediakan evaluasi terhadap kesesuaian sistem ERP dengan tujuan transformasi digital organisasi.
Project Manager	Project Manager	Memimpin implementasi HRIS sebagai bagian dari sistem ERP secara keseluruhan, memastikan integrasi berjalan lintas departemen. Menjaga agar timeline, anggaran, dan ruang lingkup proyek selaras dengan sasaran seperti sentralisasi data, otomatisasi proses, dan peningkatan visibilitas informasi SDM.

		Mengkoordinasikan komunikasi antar stakeholder teknis dan non-teknis untuk memastikan pemahaman terhadap dampak strategis dan regulatif proyek. Mengawasi pemenuhan seluruh deliverables proyek termasuk kepatuhan sistem terhadap regulasi ketenagakerjaan.
Product Manager	Product Manager	Memimpin implementasi sistem ERP dari team member project. Memastikan bahwa seluruh proses pengerjaan project berjalan sesuai dengan rencana di dalam tim.
Team Member	System Analyst	Menerjemahkan kebutuhan bisnis menjadi desain sistem teknis yang mendukung integrasi, otomatisasi alur kerja, dan pelaporan berbasis analitik. Merancang struktur data yang memungkinkan sentralisasi informasi SDM dan akurasi tinggi dalam pengelolaan data. Menyusun arsitektur sistem yang mendukung fungsi compliance, manajemen performa, dan dashboard manajerial berbasis KPI SDM. Bekerja sama dengan tim pengembang untuk memastikan desain dapat memenuhi tujuan strategis organisasi. Melakukan Quality Assurance terhadap hasil implementasi modul ERP yang dibuat.
Team Member	ERP Developer	Mendukung perancangan dan pembangunan modul ERP secara teknis sistem secara konseptual. Memberikan estimasi teknis terhadap pengembangan fitur seperti modul rekrutmen, penggajian, manajemen kinerja, dan pelaporan. Menyediakan simulasi atau mockup antarmuka pengguna berdasarkan desain yang telah disetujui untuk visualisasi kebutuhan pengguna.

		Membantu tim analis dalam menyesuaikan spesifikasi sistem agar sesuai dengan standar keamanan, compliance, dan user accessibility.

Stakeholders :

Name	Position	Contact	Internal/ External	Project Role
CFO	Chief Financial Officer	-	Internal	Project Sponsor
COO	Chief Operating Officer	-	Internal	Operation Manager
CO	Consultant	-	Internal	ERP Consultant
PM	Project Manager	-	Internal	Project Manager
SA1	System Analyst	-	Internal	Analyst from System Perspective
SA2	System Analyst	-	Internal	Analyst from System Perspective
SA3	System Analyst	-	Internal	Analyst from System Perspective

ED1	ERP Developer	-	Internal	Implement & Setup Module ERP
ED2	ERP Developer	-	Internal	Implement & Setup Module ERP
ED3	ERP Developer	-	Internal	Implement & Setup Module ERP
ED4	ERP Developer	-	Internal	Implement & Setup Module ERP
ED5	ERP Developer	-	Internal	Implement & Setup Module ERP
OP1	Operational	-	External	High Level Decisions Overall
HR1	Human Resources	-	External	High Level Decisions in HR Department
HR2	Human Resources	-	External	Head of Unit Compensation & Benefits
HR3	Human Resources	-	External	Development & Training
HR4	Human Resources	-	External	Compensation & Benefits

HR5	Human Resources	-	External	Recruitment
AT1	Accounting & Tax	-	External	Accounting & Tax Modul
AT2	Accounting	-	External	Accounting & Tax Modul

Scope Statement

Proyek implementasi *Human Resource Information System* (HRIS) dengan integrasi sistem ERP yang bertujuan untuk menyederhanakan proses HRIS melalui otomatisasi dan sentralisasi data pada suatu perusahaan manufaktur (*client*). Proyek ini menggunakan modul-modul ERP yang sudah tersedia oleh perusahaan, yang kemudian disesuaikan dan di*customize* sesuai keinginan dari perusahaan *client*. Modul-modul yang diambil terdiri dari *Employees Management*, *Time Management*, *Leave Management*, *Payroll Management*, *Resignation Management*, *Events Management*, *Recruitment Management*, *Announcements*, *Reminders*, *General Expenses*, dan *Loan Management.*

Work Breakdown Structure

Activity 1: Requirements Analysis & Planning

1.1 Kick-Off & Project Initiation

- 1.1.1 Prepare kick-off presentation and agenda
- 1.1.2 Identify and introduce key stakeholders
- 1.1.3 Define project goals, scope, constraints, and timelines

1.2 Current System & Workflow Analysis

- 1.2.1 Map current HR workflows and pain points
- 1.2.2 Conduct system gap analysis
- 1.2.3 Identify integration points with other systems

1.3 High-Level Requirement Modelling

- 1.3.1 Develop process flow diagrams (AS-IS & TO-BE)
- 1.3.2 Draft initial Functional Requirement Document (FRD)
- 1.3.3 Validate draft with department heads

1.4 Requirement Gathering

- 1.4.1 Interview HR and Legal representatives
- 1.4.2 Document Gathered Requirement
- 1.4.3 Record current system issues

1.5 Requirement Review & Clarification

1.5.1 Create detailed module-wise flowcharts

1.5.2 Validate each module's requirements with end users

1.5.3 Clarify access roles and user permission levels

1.5.4 Finalize Functional Requirement Document

1.6 Requirement Approval

1.6.1 Conduct final review meeting

1.6.2 Obtain formal sign-off from key stakeholders

Activity 2: ERP Design & Implementation

2.1 ERP Configuration & Infrastructure Setup

2.1.1 Identify required modules & features

2.1.2 Prepare data model mapping

2.1.3 Setup environments (staging, production)

2.1.4 Configure database parameters

2.2 ERP Module Implementation & Customization

2.2.1 Setup core HRIS/ERP modules

2.2.2 Configure user roles & access control

2.2.3 Configure reports and dashboards

2.3 Change Request & Continuous Improvement

2.3.1 Log & evaluate change/configuration requests

2.3.2 Perform impact analysis

2.3.3 Apply approved changes (config or minor customization)

Activity 3: System Testing & Validation

3.1 Test Planning

3.1.1 Prepare and approve System Test Plan

3.1.2 Develop test cases and scenarios

3.2 Functional & Configuration Testing

3.2.1 Conduct configuration validation testing

3.2.2 Perform end-to-end process testing

3.2.3 Log issues and adjust configurations as needed

3.3 Quality Assurance Review

- 3.3.1 Review test results and configuration completeness
- 3.3.2 Document sign-off from user and QA team

Activity 4: User Documentation & SOP Development

4.1 Create User Manuals & SOPs

- 4.1.1 Develop admin manual
- 4.1.2 Develop end-user manual
- 4.1.3 Create HR procedures documentation

4.2 UAT Preparation & Approval

- 4.2.1 Prepare UAT scenarios and test scripts for users
- 4.2.2 Conduct walkthrough and obtain sign-off from end users

Activity 5: User Training & Final UAT Validation

5.1 Training Preparation

- 5.1.1 Finalize UAT plan for organization-wide testing
- 5.1.2 Setup final test/training environment

5.2 Training Sessions

- 5.2.1 Train HR administrators
- 5.2.2 Train department managers
- 5.2.3 Train general employees

5.3 User Acceptance Validation

- 5.3.1 Execute UAT scenarios
- 5.3.2 Capture feedback and issues
- 5.3.3 Address minor changes/bug fixes
- 5.3.4 Obtain UAT sign-off

Activity 6: Deployment & Project Closure

6.1 Final Installation & Go-Live Prep

- 6.1.1 Deploy system to production environment
- 6.1.2 Confirm system readiness checklist

6.2 Project Closure

- 6.2.1 Conduct “Work Completion” meeting
- 6.2.2 Archive project documentation
- 6.2.3 Final project review & lessons learned
- 6.2.4 Obtain final sign-off

Timeline

Full Gantt Chart Linked

ERP Human Resource Management System (HRIS)						
Phase ID	Task ID	Roles	Name	Pre-Task	Start Date	End Date
1	0		**Activity 1: Requirements Analysis & Planning**	0	12-Aug-24	10-Oct-24
1	1		Kick-Off & Project Initiation	0	12-Aug-24	21-Aug-24
1	1.1		Prepare kick-off presentation and agenda	0	12-Aug-24	15-Aug-24
1	1.2		Identify and introduce key stakeholders	0	12-Aug-24	15-Aug-24
1	1.3		Define project goals, scope, constraints, and timelines	1.1.1, 1.1.2	16-Aug-24	21-Aug-24
1	2		Current System & Workflow Analysis	1.1	22-Aug-24	26-Aug-24
1	2.1		Map current HR workflows and pain points	1.1	22-Aug-24	26-Aug-24
1	2.2		Conduct system gap analysis	1.1	22-Aug-24	26-Aug-24
1	2.3		Identify integration points with other systems	1.1	22-Aug-24	26-Aug-24
1	3		High-Level Requirement Modelling	1.2	27-Aug-24	4-Sep-24
1	3.1		Develop process flow diagrams (AS-IS & TO-BE)	1.2	27-Aug-24	29-Aug-24
1	3.2		Draft initial Functional Requirement Document (FRD)	1.3.1	30-Aug-24	2-Sep-24
1	3.3		Validate draft with department heads	1.3.2	2-Sep-24	4-Sep-24
1	4		Requirement Gathering – Session A (HR Core Functions, Legal, Compliance, Existing Issues)	1.3	5-Sep-24	21-Sep-24
1	4.1		Interview HR and Legal representatives	1.3	5-Sep-24	11-Sep-24
1	4.2		Document Gathered Requirement	1.4.1	12-Sep-24	18-Sep-24
1	4.3		Record current system issues	1.4.1	19-Sep-24	21-Sep-24
1	5		Requirement Review & Clarification	1.4	23-Sep-24	5-Oct-24
1	5.1		Create detailed module-wise flowcharts	1.4	23-Sep-24	30-Sep-24
1	5.2		Validate each module's requirements with end users	1.5.1	1-Oct-24	3-Oct-24

1	5.3		Clarify access roles and user permission levels	1.5.1	1-Oct-24	3-Oct-24
1	5.4		Finalize Functional Requirement Document	1.5.2, 1.5.3	4-Oct-24	5-Oct-24
1	6		Requirement Approval	1.5	7-Oct-24	10-Oct-24
1	6.1		Conduct final review meeting	1.5	7-Oct-24	8-Oct-24
1	6.2		Obtain formal sign-off from key stakeholders	1.6.1	9-Oct-24	10-Oct-24
2	0		**Activity 2 : ERP Design & Implementation**	1	11-Oct-24	26-Dec-24
2	1		ERP Configuration & Infrastructure Setup	1	11-Oct-24	4-Nov-24
2	1.1		Identify required modules & features	1	11-Oct-24	16-Oct-24
2	1.2		Prepare data model mapping	2.1.1	17-Oct-24	23-Oct-24
2	1.3		Setup environments (staging, production)	2.1.2	24-Oct-24	30-Oct-24
2	1.4		Configure database parameters	2.1.3	31-Oct-24	4-Nov-24
2	2		ERP Module Implementation & Customization	2.1	5-Nov-24	26-Nov-24
2	2.1		Setup core HRIS/ERP modules	2.1	5-Nov-24	19-Nov-24
2	2.2		Configure user roles & access control	2.2.1	20-Nov-24	22-Nov-24
2	2.3		Configure reports and dashboards	2.2.2	23-Nov-24	26-Nov-24
2	3		Change Request & Continuous Improvement	2.2	27-Nov-24	26-Dec-24
2	3.1		Log & evaluate change/configuration requests	2.2	27-Nov-24	10-Dec-24
2	3.2		Perform impact analysis	2.3.1	11-Dec-24	17-Dec-24
2	3.3		Apply approved changes (config or minor customization)	2.3.2	18-Dec-24	26-Dec-24
3	0		**Activity 3: System Testing & Validation**	2	27-Dec-24	29-Jan-25
3	1		Test Planning	2	27-Dec-24	6-Jan-25
3	1.1		Prepare and approve System Test Plan	2	27-Dec-24	6-Jan-25
3	1.2		Develop test cases and scenarios	2	27-Dec-24	6-Jan-25
3	2		Functional Testing & Configuration Testing	3.1	7-Jan-25	22-Jan-25
3	2.1		Conduct configuration validation testing	3.1	7-Jan-25	10-Jan-25
3	2.2		Perform end-to-end process testing	3.2.1	11-Jan-25	16-Jan-25
3	2.3		Log issues and adjust configurations as needed	3.2.2	17-Jan-25	22-Jan-25

3	3		Quality Assurance Review	3.2	23-Jan-25	29-Jan-25
3	3.1		Review test results and configuration completeness	3.2	23-Jan-25	27-Jan-25
3	3.2		Document sign-off from user and QA team	3.3.1	28-Jan-25	29-Jan-25
4	0		**Activity 4: User Documentation & SOP Development**	3	30-Jan-25	25-Feb-25
4	1		Create User Manuals & SOPs	3	30-Jan-25	18-Feb-25
4	1.1		Develop admin manual	3	30-Jan-25	5-Feb-25
4	1.2		Develop employee user manual	4.1.1	6-Feb-25	11-Feb-25
4	1.3		Create HR procedures documentation	4.1.2	12-Feb-25	18-Feb-25
4	2		UAT Preparation & Approval	4.1	19-Feb-25	25-Feb-25
4	2.1		Prepare UAT scenarios and test scripts for users	4.1	19-Feb-25	22-Feb-25
4	2.2		Conduct walkthrough and obtain sign-off from end users	4.2.1	24-Feb-25	25-Feb-25
5	0		**Activity 5: User Training & Final UAT Validation**	4	26-Feb-25	29-Mar-25
5	1		Training Preparation	4	26-Feb-25	5-Mar-25
5	1.1		Finalize UAT plan for organization-wide testing	4	26-Feb-25	1-Mar-25
5	1.2		Setup final test/training environment	5.1.1	3-Mar-25	5-Mar-25
5	2		Training Sessions	5.1	6-Mar-25	12-Mar-25
5	2.1		Train HR administrators	5.1	6-Mar-25	8-Mar-25
5	2.2		Train department managers	5.1	6-Mar-25	8-Mar-25
5	2.3		Train general employees	5.2.2, 5.2.3	10-Mar-25	12-Mar-25
5	3		User Acceptance Validation	5.2	13-Mar-25	29-Mar-25
5	3.1		Execute UAT scenarios	5.2	13-Mar-25	19-Mar-25
5	3.2		Capture feedback and issues	5.3.1	20-Mar-25	22-Mar-25
5	3.3		Address minor changes/bug fixes	5.3.2	24-Mar-25	26-Mar-25
5	3.4		Obtain UAT sign-off	5.3.3	27-Mar-25	29-Mar-25
6	0		**Activity 6: Deployment & Project Closure**	5	31-Mar-25	10-Apr-25
6	1		Final Installation & Go-Live Prep	5	31-Mar-25	3-Apr-25
6	1.1		Deploy system to production environment	5	31-Mar-25	3-Apr-25

6	1.2		Confirm System readiness checklist	5	31-Mar-25	3-Apr-25
6	2		Project Clousure	6.1	4-Apr-25	10-Apr-25
6	2.1		Conduct “Work Completion” meeting	6.1	4-Apr-25	7-Apr-25
6	2.2		Archive project documentation	6.1	4-Apr-25	8-Apr-25
6	2.3		Final project review & lessons learned	6.1	4-Apr-25	9-Apr-25
6	2.4		Obtain Final sign-off	6.2.1, 6.2.2, 6.2.3	9-Apr-25	10-Apr-25

RACI

Activity	**Chief Financial Officer**	**Chief Operating Officer**	**Consultant**	**Project Manager**	**Product Manager**	**System Analyst**	**Programmer**
Activity 1: Requirements Analysis & Planning		I	R	C	A	R	I
Activity 2: ERP Design & Implementation		I	A	C	C	R	R
Activity 3: System Testing & Validation	I	I	C	C	A	R	I
Activity 4: User Documentation & SOP Development		I	C	C	A	R	I
Activity 5: User Training & Final UAT Validation		I	C	C	A	R	I

Activity 6: Deployment & Project Closure		I	C	A, R	I	I	R

Histogram

Resource Histogram

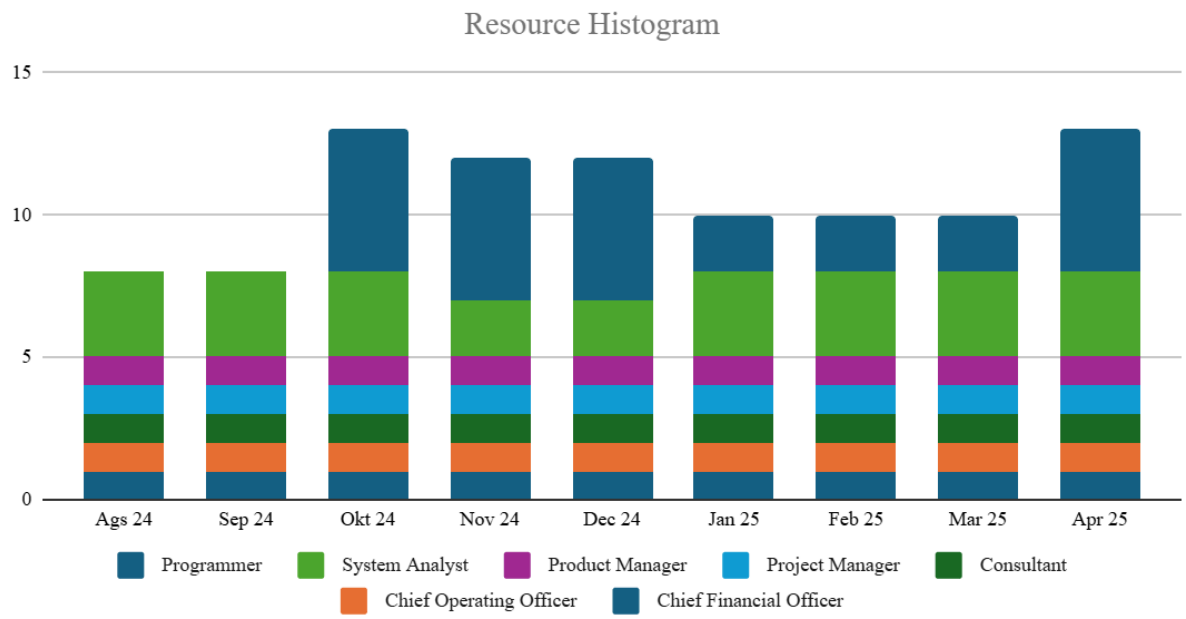

Budgeting (ERP - HRIS)

Rp.500.000.000

Items	Cost/Unit/Month	Quantity	Month	Sub-totals level 2	Sub-totals level 1	% of Totals
1. Project Management					**Rp. 344.000.000,00**	68,8%
Consultant	Rp. 15.000.000,00	1	8	Rp. 120.000.000,00		
Project Manager	Rp. 12.000.000,00	1	8	Rp. 96.000.000,00		
Business Analyst	Rp. 5.000.000,00	3	8	Rp. 40.000.000,00		
System Analyst	Rp. 5.000.000,00	3	8	Rp. 40.000.000,00		
Programmer	Rp. 8.000.000,00	5	6	Rp. 48.000.000,00		
2. Hardware					**Rp. 45.000.000,00**	9%
Server	Rp. 2.500.000,00	2	8	Rp. 40.000.000,00		
Storage	Rp. 625.000,00	1	8	Rp. 5.000.000,00		
3. Software					**Rp. 16.000.000,00**	3,2%
Licensed Software	Rp. 2.000.000,00	1	8	Rp. 16.000.000,00		
4. Testing					**Rp. 10.000.000,00**	2%
5. Training & Support					**Rp. 20.000.000,00**	4%

6. Contingency Reserves					**Rp. 50.000.000,00**	10%
Substitutes Team Member				Rp. 30.000.000,00		
Hardware/Software Risk				Rp. 20.000.000,00		
7. Management Reserves					**Rp. 15.000.000,00**	3%
Total Project Cost Estimate					**Rp. 500.000.000,00**	100%

Organization Structure

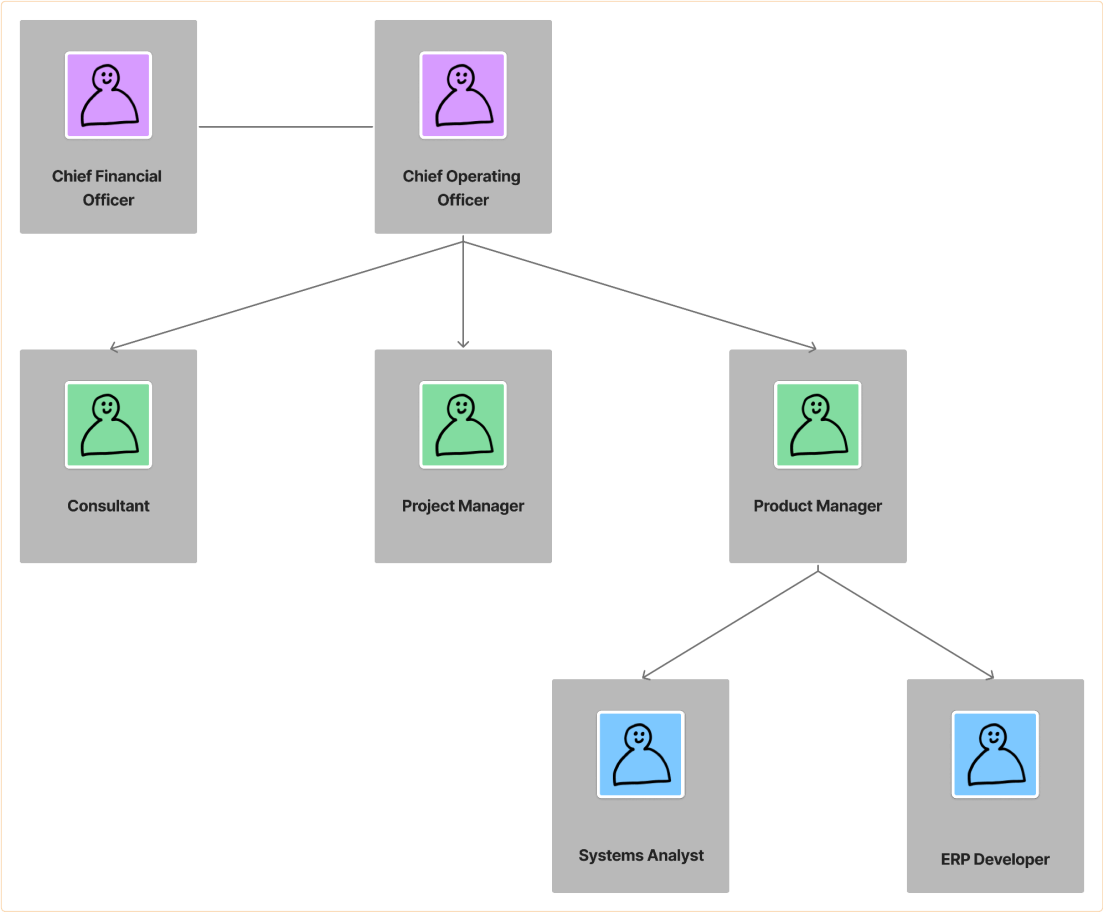

Risk Management/Risk Plan

- **Risk Register-Ranking**

Risk ID	Rank	Description	Category	Root Cause	Trigger	Potential Response	Risk Owner	Probability	Impact	Risk Score	Risk Level
Internal											
R01	1	Estimasi waktu dan biaya tidak akurat	Project Management	Estimasi terlalu optimistis, kurang data historis	Proyek molor atau overbudget	Mitigate, Contigency Plan	Project Manager	High	High	9	Extreme
R02	2	Tim implementasi tidak kompeten	Organizational	Kurangnya pelatihan teknis	kinerja tim lambat atau salah konfigurasi	Mitigate	Project Manager	Medium	High	6	High
R03	2	Pemahaman bisnis klien tidak cukup	Business	Kurangnya eksplorasi proses bisnis awal	Solusi tidak sesuai kebutuhan klien	Mitigate	Business Analyst	Medium	High	6	High
R04	3	Komunikasi internal vendor tidak lancar	Organizational	Tidak ada tools kolaborasi efektif atau SOP komunikasi	Task overlap, miskomunikasi	Mitigate	Project Manager	Medium	Medium	4	Medium
R05	2	Risiko reputasi bila proyek gagal	Business	Kurangnya mitigasi risiko besar, gagal deliverables	Klien menyebarkan review negatif	Contingency Plan, Accept	Product Manager	Medium	High	6	High
R06	2	Benturan resource internal	Organizational	Tim ditugaskan di banyak proyek sekaligus	Proyek terlambat atau tidak fokus	Mitigate	Project Manager	Medium	High	6	High
R07	4	Sistem tidak sesuai regulasi lokal	Technical	Sistem tidak update dengan UU ketenagakerjaan/pajak	Ketidaksesuaian pelaporan pajak	Avoid, Mitigate	Product Manager	Low	High	3	Low

				terbaru							
R08	4	Risiko hukum dari wanprestasi	Business	Kontrak menjabarkan ekspektasi atau deliverables dengan jelas	Klien menuntut secara hukum	Mitigate, Transfer	Consultant	Low	High	3	Low
External											
R09	1	Kurangnya dukungan manajemen	Organizational	Manajemen tidak terlibat aktif	Proyek terhambat karena keputusan tertunda	Mitigate	Project Sponsor (Klien)	High	High	9	Extreme
R10	1	Penolakan dari user/karyawan	Organizational	Perubahan budaya kerja	User menolak sistem baru	Mitigate	HR (Klien)	High	High	9	Extreme
R11	1	Permintaan tambahan (scope creep)	Project Management	Harapan tidak dibatasi sejak awal	Penambahan fitur.fungsi terus-menerus	Avoid, Mitigate	HR (Klien)	High	High	9	Extreme
R12	1	Kualitas data yang buruk	Technical	Data lama tidak valid/duplikat	Migrasi gagal atau error output sistem	Mitigate	HR/IT (Klien)	High	High	9	Extreme
R13	2	Keterlambatan penyediaan data	Organizational	Klien tidak siap atau tidak disiplin jadwal	Aktivitas setup tertunda	Mitigate	HR (Klien)	High	Medium	6	High
R14	2	Gangguan operasional saat go-live	Technical	Tidak ada sistem paralel	Proses HR terganggu	Contigency Plan	HR (Klien)	Medium	High	6	High
R15	2	Gagal integrasi sistem	Technical	Tidak ada dokumentasi atau keterbatasan API	Sistem HR tidak terhubung dengan payroll/absensi	Mitigate, Contigency Plan	HR/IT (Klien)	Medium	High	6	High
R16	2	Perubahan struktur organisasi	Organizational	Restrukturisasi, PHK, merger	Tim proyek terganggu, kebutuhan berubah	Accept, Contigency Plan	HR/Operasional (Klien)	Medium	High	6	High

- **Risk Matrices**

	Low (1)	Medium (2)	High (3)	**Impact**
Low (1)	Low (1)	Low (2)	Low (3)	

Medium (2)	Low (2)	Medium (4)	Medium (6)
High (3)	Low (3)	Medium (6)	Extreme (9)

Probability

Stakeholder Registers

Name	Position	Contact	Internal/External	Project Role
CFO	Chief Financial Officer	-	Internal	Project Sponsor
COO	Chief Operating Officer	-	Internal	Operation Manager
CO	Consultant	-	Internal	ERP Consultant
PM	Project Manager	-	Internal	Project Manager
PR	Product Manager	-	Internal	Product Manager
SA1	System Analyst	-	Internal	Analyst from System Perspective

SA2	System Analyst	-	Internal	Analyst from System Perspective
SA3	System Analyst	-	Internal	Analyst from System Perspective
ED1	ERP Developer	-	Internal	Implement & Setup Module ERP
ED2	ERP Developer	-	Internal	Implement & Setup Module ERP
ED3	ERP Developer	-	Internal	Implement & Setup Module ERP
ED4	ERP Developer	-	Internal	Implement & Setup Module ERP
ED5	ERP Developer	-	Internal	Implement & Setup Module ERP
OP1	Operational	-	External	High Level Decisions Overall
HR1	Human Resources	-	External	High Level Decisions in HR Department

HR2	Human Resources	-	External	Head of Unit Compensation & Benefits
HR3	Human Resources	-	External	Development & Training
HR4	Human Resources	-	External	Compensation & Benefits
HR5	Human Resources	-	External	Recruitment
AT1	Accounting & Tax	-	External	Accounting & Tax Modul
AT2	Accounting & Tax	-	External	Accounting & Tax Modul

Stakeholder Analysis

Position	Internal/External	Influence	Engagement Level	Project Role
Chief Financial Officer	Internal	Medium	Neutral	Project Sponsor
Chief Operating Officer	Internal	High	Leading	Operation Manager
Project Manager	Internal	High	Leading	Project Manager

Product Manager	Internal	High	Leading	Product Manager
System Analyst	Internal	Medium	Supportive	Analyst from System Perspective
ERP Developer	Internal	Medium	Supportive	Implement & Setup Module ERP
Operational	External	High	Leading	High Level Decisions Overall
Human Resources	External	High	Supportive	Validate Module HR Requirement
Accounting & Tax	External	High	Supportive	Validate Module Accounting & Tax Requirement
